










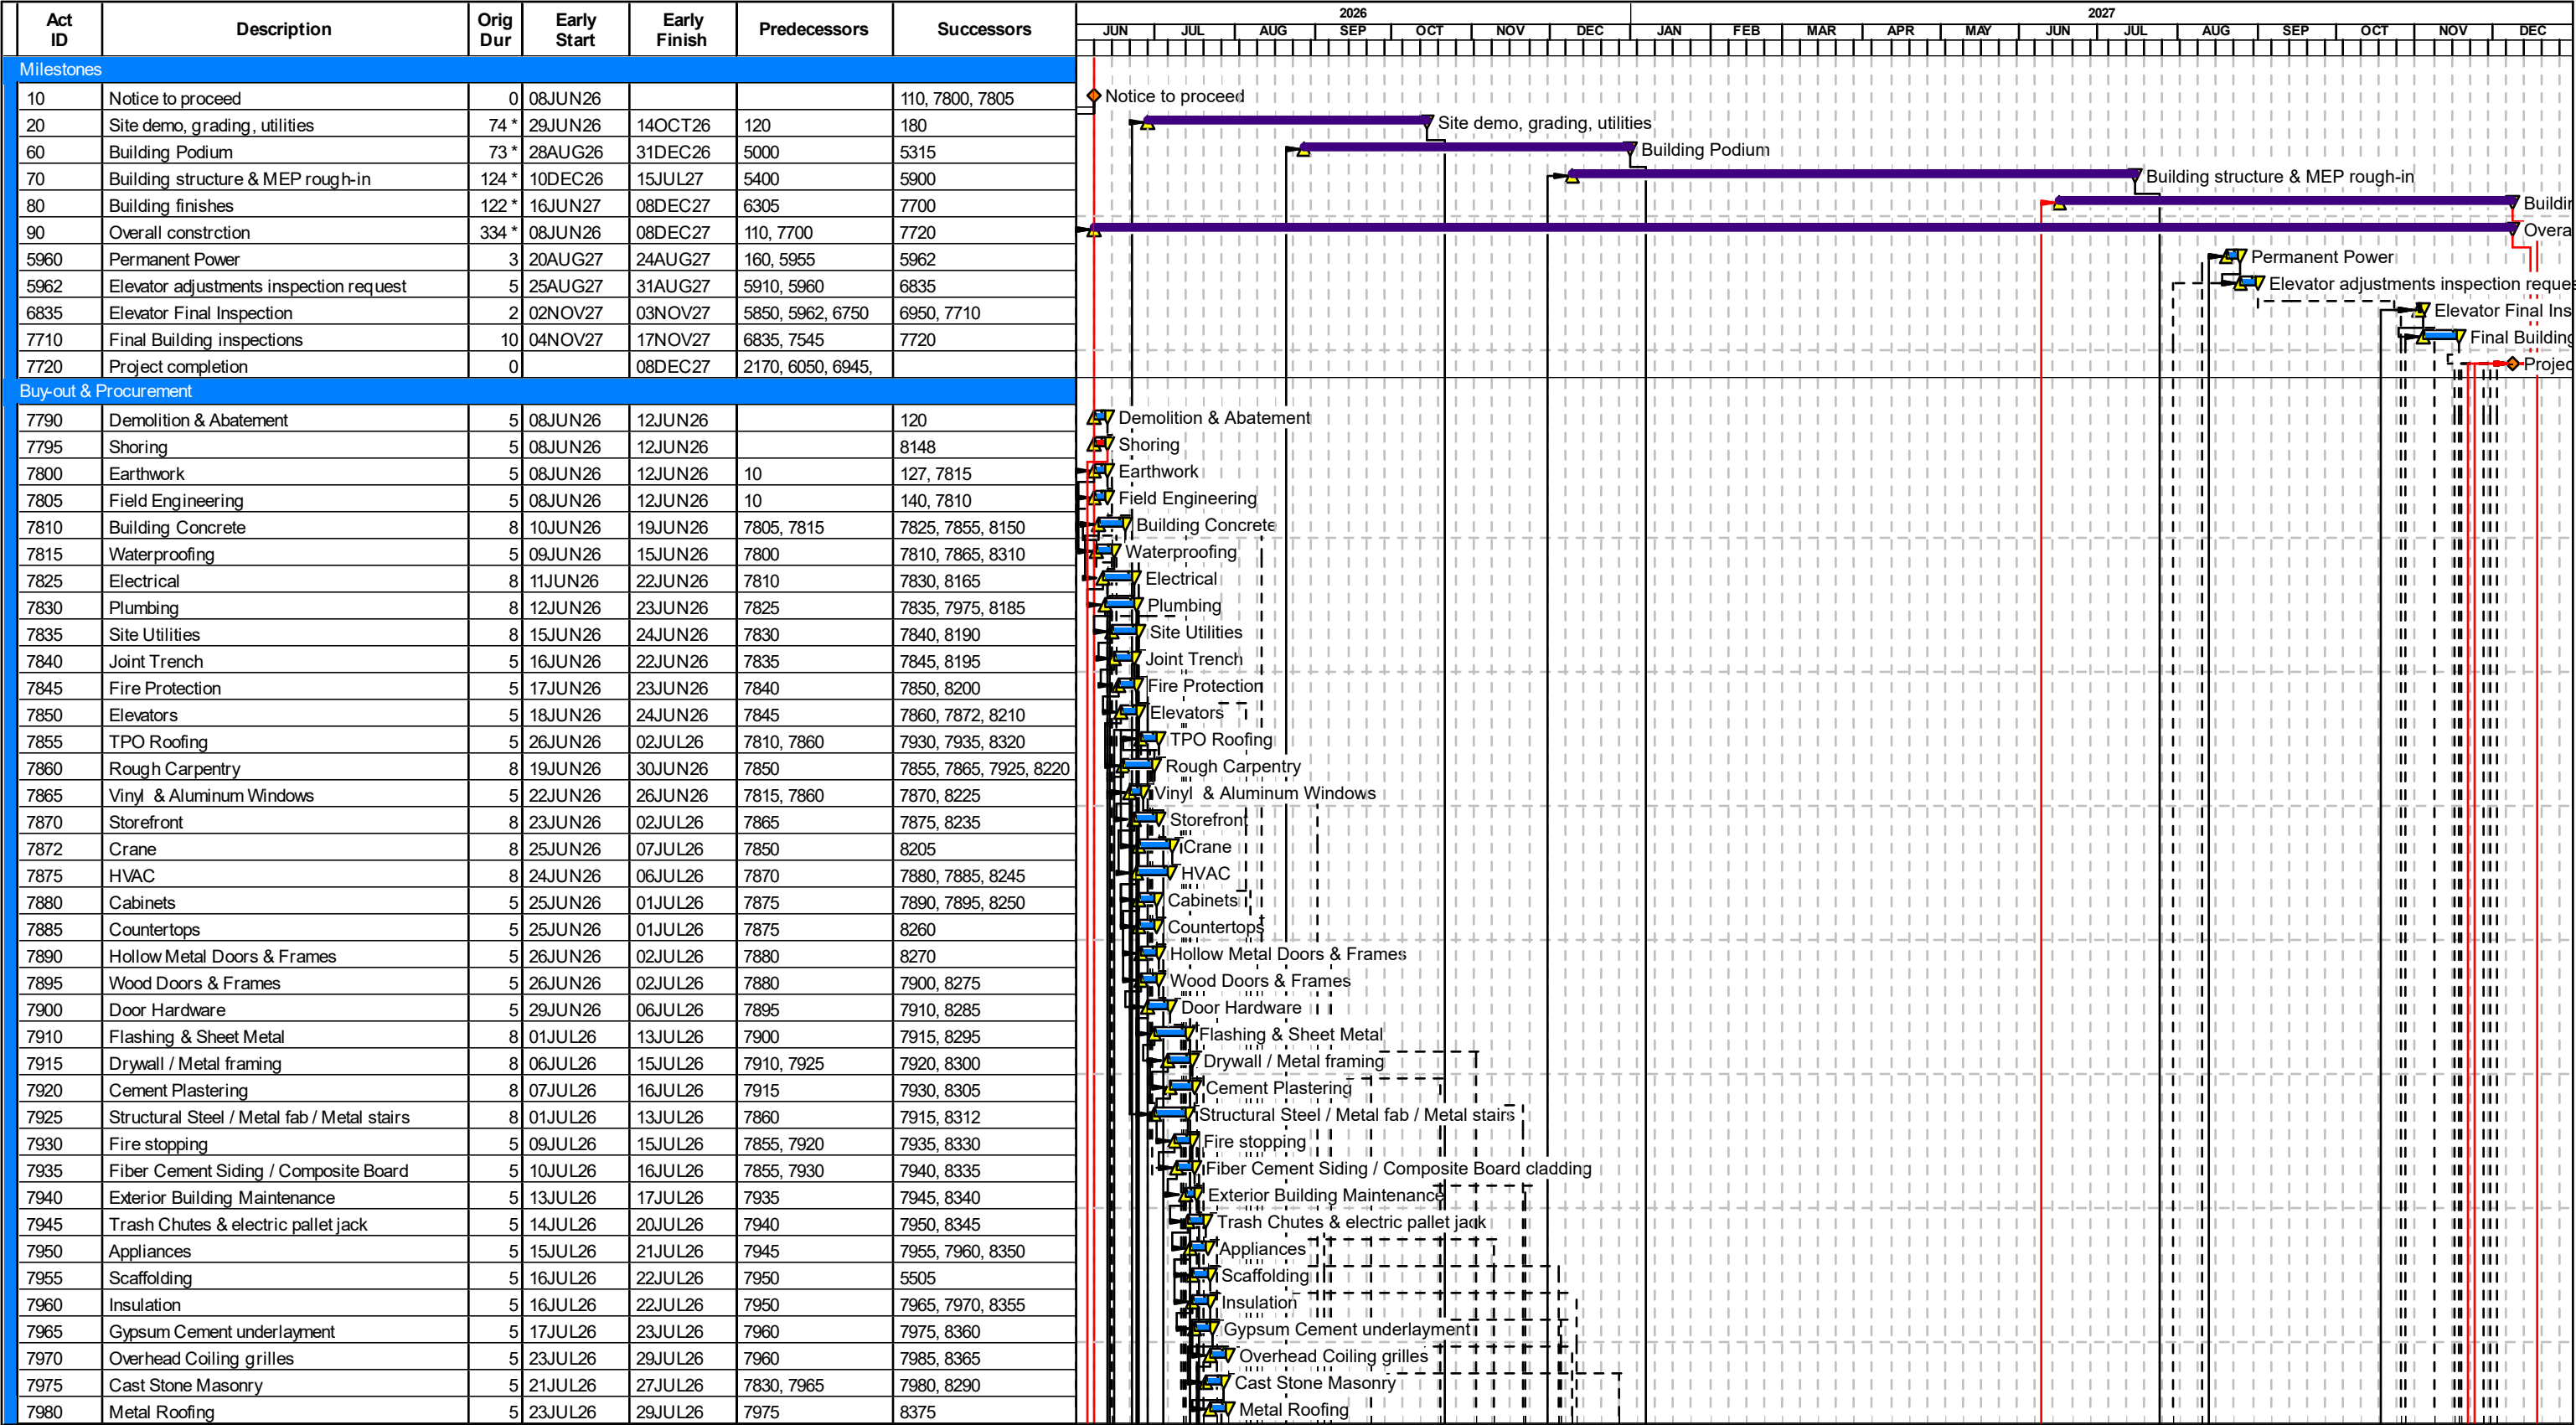

Act ID

Description

Orig Dur

Early Start

Early Finish

Predecessors

Successors

5030

Rebar template

2

02OCT26

05OCT26

5025

5035

5035

Wall / Column dowels

2

13OCT26

14OCT26

5025, 5030

5040

5040

Pour pour East mat

1

15OCT26

15OCT26

5035, 5050, 8162

5055, 5078

5045

Elevator pit slab

3

11SEP26

15SEP26

5002, 8310

5050

5050

Form & pour elevator pit walls

3

16SEP26

18SEP26

5045

5010, 5040

5055

Backform walls - shoot 1

4

16OCT26

22OCT26

5040

5060, 5071

5060

Wall reinforcing

4

20OCT26

26OCT26

5055, 8155

5062, 5065, 5072

5062

Wire / Inspect

1

27OCT26

27OCT26

5060

5065

5065

Shoot walls

2

29OCT26

30OCT26

5060, 5062

5070

5070

Strip backforms

2

02NOV26

03NOV26

5065

5180

5071

Backform walls - shoot 2

4

23OCT26

29OCT26

5055

5072

5072

Wall reinforcing

4

27OCT26

02NOV26

5060, 5071

5073, 5075

5073

Wire / Inspect

1

03NOV26

03NOV26

5072

5075

5075

Shoot walls

1

03NOV26

03NOV26

5072, 5073

5076

5076

Strip backforms

2

05NOV26

06NOV26

5075

5220

5078

Column Reinforcing - pour 1

2

16OCT26

19OCT26

5040

5080, 5095

5080

Column Forms

3

20OCT26

23OCT26

5078

5085, 5100

5085

Pour columns

1

26OCT26

26OCT26

5080

5090

5090

Strip column forms

1

27OCT26

27OCT26

5085

5100, 5220

5095

Column Reinforcing - pour 2

2

20OCT26

22OCT26

5078

5100, 5200

5100

Column Forms

3

29OCT26

02NOV26

5080, 5090, 5095

5105

5105

Pour columns

1

03NOV26

03NOV26

5100

5110

5110

Strip column forms

1

05NOV26

05NOV26

5105

5205

5115

Lay-out mat preimeter / elevator pit - West

3

02SEP26

08SEP26

5000

5120, 5125

5120

Excavate elevator pit & plumbing

5

11SEP26

17SEP26

5002, 5115

5125, 5140, 5160

5125

Underslab Plumbing and electrical

7

21SEP26

29SEP26

5005, 5115, 5120

5130

5130

Clean/ regrade subgrade

2

01OCT26

02OCT26

5125, 5165

5135

5135

Agg base and underslab vapor barrier

2

05OCT26

06OCT26

5130

5140

5140

Mat reinforcing - West

7

13OCT26

22OCT26

5025, 5120, 5135

5145, 5150

5145

Rebar template

2

15OCT26

16OCT26

5140, 5165

5150

5150

Wall / Column dowels

2

23OCT26

26OCT26

5140, 5145

5155

5155

Pour pour East mat

1

27OCT26

27OCT26

5150, 5165

5180, 5200

5160

Elevator pit slab

3

18SEP26

22SEP26

5120

5165

5165

Form & pour elevator pit walls

3

23SEP26

25SEP26

5160

5130, 5145, 5155

5180

Backform walls - Shoot 3

3

05NOV26

09NOV26

5070, 5155

5182

5182

Wall reinforcing

3

09NOV26

12NOV26

5180

5184, 5186

5184

Wire / Inspect

1

13NOV26

13NOV26

5182

5186

5186

Shoot walls

2

16NOV26

17NOV26

5182, 5184

5188

5188

Strip backforms

2

19NOV26

20NOV26

5186

5275

5200

Column Reinforcing - pour 3

2

29OCT26

30OCT26

5095, 5155

5205

5205

Column Forms

2

06NOV26

09NOV26

5110, 5200

5210

5210

Pour columns

1

10NOV26

10NOV26

5205

5215

5215

Strip column forms

1

12NOV26

12NOV26

5210

5275

5220

Form PT Slab East - level 2 (incl beam)

8

09NOV26

20NOV26

5076, 5090

5225, 5235, 5275

5225

Lay-out Deck forms

4

13NOV26

19NOV26

5220

5230, 5235, 5240

5230

M,P & E cans

4

17NOV26

23NOV26

5225

5235

5235

Rebar & Cables (incl beam)

7

20NOV26

04DEC26

5220, 5225, 5230,

5245, 5290

5240

Set Embeds

2

20NOV26

23NOV26

5225

5245

5245

Pour PT Slab -East level 2

1

07DEC26

07DEC26

5235, 5240

5250, 5270

5250

Slab Cure

6

08DEC26

13DEC26

5245

5255

5255

Stress cables

2

14DEC26

15DEC26

5250, 8590

5260, 5265, 5370,

5260

Drop slab forms

3

17DEC26

21DEC26

5255

2015, 5315, 5330, 5395

Start date

08JUN26

Finish date

08DEC27

Data date

08JUN26

Run date

12MAR26

Page number

5A

© Primavera Systems, Inc.

James E. Roberts - Obayashi Corp.

Ephesian Legacy Court

Early bar

Early start point

Early finish point

Progress bar

Critical bar

Summary bar

Start milestone point

Finish milestone point













[illegible]

[illegible]











